DISTRICT	COUNTY	ROUTE	SECTION	SHEET
8-0	YORK	–	BRG	1 OF 1
DOVER TOWNSHIP				

REVISION NUMBER	REVISIONS	DATE	BY

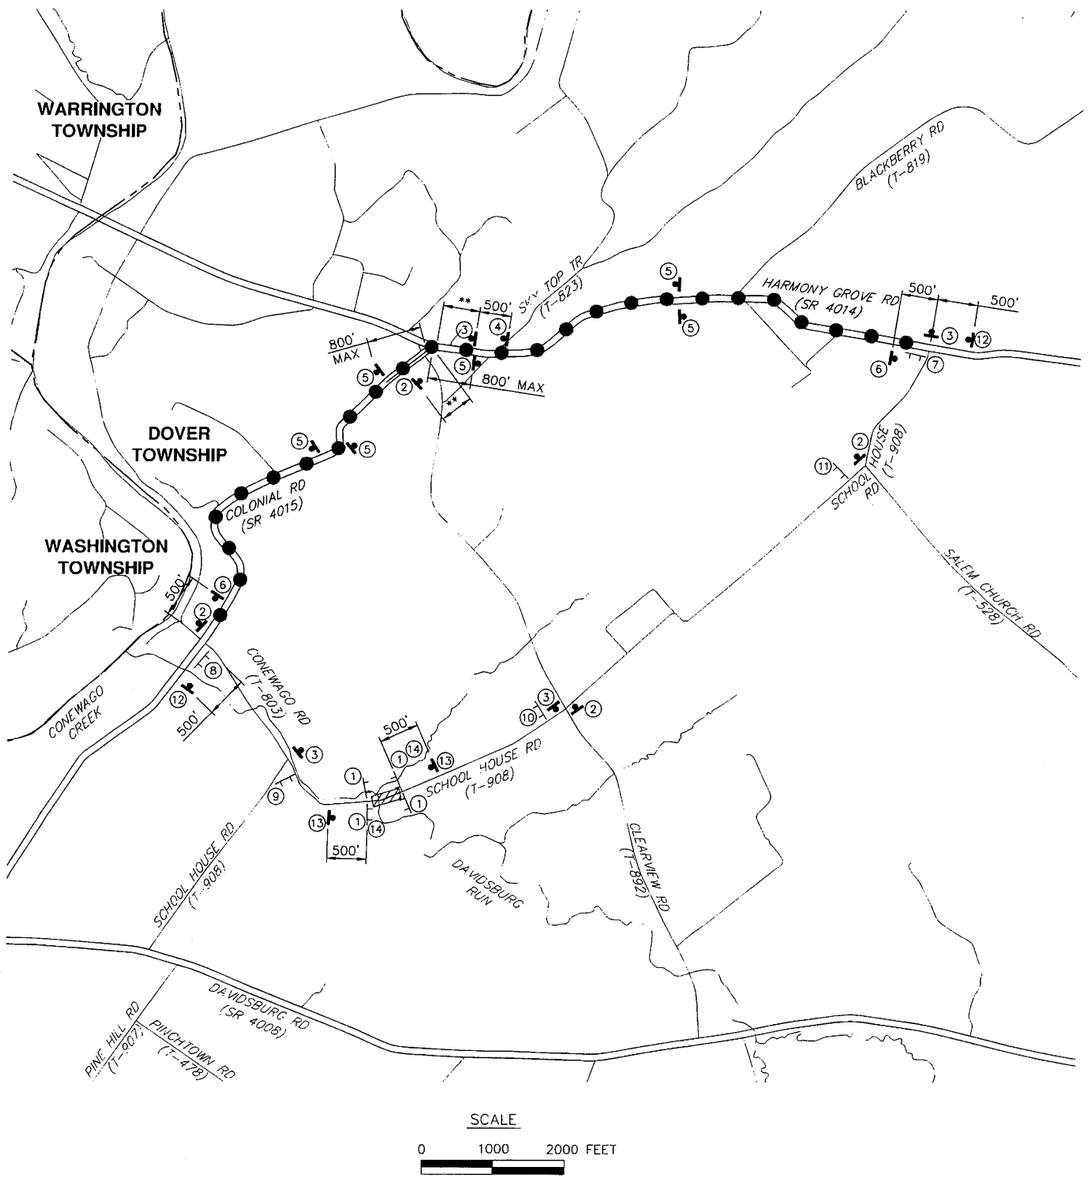

LEGEND OF SIGNS AND DEVICES

NO.	LEGEND	SERIES	SIZE	MOUNTING	QUANTITY	REMARKS
1	BRIDGE CLOSED	R11-2-1	48"X30"	TYPE III BARRICADE	4	BARRICADES MUST EXTEND ACROSS FULL WIDTH OF SCHOOL HOUSE RD. DO NOT BLOCK ADJACENT DRIVEWAY.
2	SCHOOL HOUSE RD / DETOUR →	SP-1 M4-9R	42"X14" 30"X24"	TYPE B	4	
3	SCHOOL HOUSE RD / DETOUR ←	SP-1 M4-9L	42"X14" 30"X24"	TYPE B	4	
4	SCHOOL HOUSE RD / DETOUR ↰	SP-1 M4-9SL	42"X14" 30"X24"	TYPE B	1	
5	SCHOOL HOUSE RD / DETOUR ↑	SP-1 M4-9S	42"X14" 30"X24"	TYPE B	6	
6	SCHOOL HOUSE RD / END DETOUR	SP-1 M4-8A	42"X14" 24"X18"	TYPE B	2	
7	SCHOOL HOUSE RD / ROAD CLOSED TO THRU TRAFFIC / DETOUR	SP-1 R11-4 M4-10R	42"X14" 60"X30" 48"X18"	TYPE III BARRICADE	1	PLACE ON RIGHT SIDE OF SCHOOL HOUSE RD AT THE INTERSECTION OF HARMONY GROVE RD
8	SCHOOL HOUSE RD / ROAD CLOSED TO THRU TRAFFIC / DETOUR	SP-1 R11-4 M4-10L	42"X14" 60"X30" 48"X18"	TYPE III BARRICADE	1	PLACE ON RIGHT SIDE OF SCHOOL HOUSE RD AT THE INTERSECTION OF COLONIAL RD
9	BRIDGE OUT 1/4 MILE AHEAD LOCAL TRAFFIC ONLY	R11-3B R11-3A	48"X12" 60"X30"	TYPE III BARRICADE	1	PLACE ON RIGHT SIDE OF SCHOOL HOUSE RD.
10	BRIDGE OUT 1/2 MILE AHEAD LOCAL TRAFFIC ONLY	R11-3B R11-3A	48"X12" 60"X30"	TYPE III BARRICADE	1	PLACE ON RIGHT SIDE OF SCHOOL HOUSE RD.
11	BRIDGE OUT 1 1/2 MILE AHEAD LOCAL TRAFFIC ONLY	R11-3B R11-3A	48"X12" 60"X30"	TYPE III BARRICADE	1	PLACE ON RIGHT SIDE OF SCHOOL HOUSE RD.
12	SCHOOL HOUSE RD / DETOUR AHEAD	SP-1 W20-2 W30-1-6	42"X14" 36"X36" 20"X6"	TYPE B	2	
13	ROAD CLOSED 500 FT	W20-3 W30-1-1	36"X36" 20"X6"	TYPE B	2	
14*	THIS BRIDGE TO BE CLOSED FOR CONSTRUCTION < DATE >	W23-101	96"X48"	TYPE III BARRICADE	2	PLACE ON RIGHT SIDE OF SCHOOL HOUSE RD

GENERAL NOTES

DETOUR IS IN ACCORDANCE WITH PATA 215 OF PUBLICATION 213.

FURNISH, ERECT, PLACE AND MAINTAIN TRAFFIC CONTROL SIGNS AND DEVICES. MAINTAIN TRAFFIC DURING HOURS OF CONSTRUCTION AND AT ALL OTHER TIMES IN ACCORDANCE WITH THE METHODS INDICATED ON THESE DRAWINGS AND THE FOLLOWING:

1. THE SPECIAL PROVISIONS OF THE CONTRACT.
2. THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (MUTCD).
3. PENNDOT PUBLICATION 212, OFFICIAL TRAFFIC CONTROL DEVICES, SUBCHAPTER E.
4. PENNDOT PUBLICATION 213, TEMPORARY TRAFFIC CONTROL GUIDELINES.
5. PENNDOT PUBLICATION 35, APPROVED CONSTRUCTION MATERIALS (BULLETIN 15).
6. PENNDOT PUBLICATION 408, SPECIFICATIONS.
7. PENNDOT PUBLICATION 111, TRAFFIC CONTROL PAVEMENT MARKINGS AND SIGNING STANDARDS, TC-8600 AND TC-8700 SERIES.
8. PENNDOT PUBLICATION 236 HANDBOOK OF APPROVED SIGNS.

CONTRACTOR SHALL COOPERATE AND COORDINATE WITH ANY ADJACENT CONTRACTOR IN THE MAINTENANCE AND PROTECTION OF TRAFFIC DURING CONSTRUCTION. COORDINATE THE PLACEMENT, COVERING, AND/OR REMOVAL OF SIGNS AND TRAFFIC CONTROL DEVICES THROUGHOUT THE DURATION OF THIS CONTRACT.

DETOUR WILL LAST APPROXIMATELY 180 CALENDAR DAYS.

SP-1

SP-1 REQUIRED IF BRIDGE 166 & DOVER TOWNSHIP BRIDGE 424 DETOURS ARE CONCURRENTLY IN PLACE AT ANY GIVEN TIME.



NOT TO SCALE

BACKGROUND – ORANGE PRISMATIC SHEETING
LEGEND – BLACK NON-REFLECTIVE
4" UPPERCASE LETTERING SERIES E

LINE 1:	LINE 2:
SPACE – 9.25"	SPACE – 5.4"
S – 4.0"	H – 4.2"
C – 4.0"	O – 4.3"
H – 4.2"	U – 4.2"
O – 4.1"	S – 4.2"
O – 4.3"	E – 2.9"
L – 2.9"	SPACE – 4.0"
SPACE – 9.25"	R – 4.2"
	D – 3.2"
	SPACE – 5.4"
	TOTAL = 42"

LEGEND

- WORK ZONE
- DETOUR ROUTE
- STATE ROAD
- LOCAL ROAD
- MUNICIPALITY BOUNDARY
- STREAMS, CREEKS & RIVERS
- (1) SIGN / TYPE B POST
- (1) SIGN / TYPE III MOUNTING

SIGN NOTES:

* TO BE INSTALLED TWO (2) WEEKS PRIOR TO IMPLEMENTING THE DETOUR AND REMOVED ONCE DETOUR IS IN PLACE.

** PLACE SIGN AS CLOSE TO INTERSECTION AS PRACTICAL, BUT NO MORE THAN 800' AWAY.

DETOUR LENGTH = 2.5 MILES

YORK COUNTY BRIDGE 166 – (T-819) TEMPORARY TRAFFIC CONTROL PLAN

HERBERT, ROWLAND & GRUBIC, INC.
369 EAST PARK DRIVE
HARRISBURG, PA 17111

COMMONWEALTH OF PENNSYLVANIA REGISTERED PROFESSIONAL BRIAN L. GUERSON JR. ENGINEER PE083651

09/12/2022

DES: BSB	DWG: BSB	CKD: JBL | EJS

PLOTTED: Sep 12, 2022-9:41am
OPERATOR: ttannahill
FILE NAME: \\192.168.0.34\Project\0037\003721_0434\C3D\Plan Sets\DETOUR\DETOUR PLAN - BR 166.dwg Layout: TCP
